

Item No.	Qty.	Catalog Number / Details
066-00	1	Designation: 1EH1 - 1EL1 INTEGRATED SOLUTIONS Square D Integrated Power Center Designation: 1EH1 - 1EL1 Tested In Accordance With UL 891 Accessibility: Front Enclosure: Type 1 Seismically Qualified Shipping splits: Square D Preference Phenolic White Surface / Black Letters Nameplate Total Number of Sections: 1 Release - 3/1/2016, Processed - 6/7/2016 2:10:11 PM Section 1 2 cells over 1 cell Transformer Combo Section Width: 42 in Section Depth: 24 in Section Height: 91.5 in ANSI 49 Gray No section to left (closed end) Orders containing 15 or more INEQ sections may be delivered in staggered shipments: 10 units based on the product lead time, with 10 additional units each week after, until order is complete. Contact Salisbury customer service to prioritize shipments. Designation: 1EH1 NF Panel Interior Location: Top Left - Section 1 480Y/277V 3Ph 4W 60Hz AIR: 35k System Protection: Fully Rated Main Lugs: 225A Aluminum/Copper lugs Mechanical Lugs Bus Bar: Copper Hinged trim Ground Bar: Standard Copper Door Lock w/keys Neutral: Copper Included SPD Surge Suppression Peak Surge Rating: 100 kA With Dry Contacts With Surge Counter Fed from Cable by others - Bottom Phenolic White Surface / Black Letters Nameplate Branch Breakers (1) 45A 3P C/B - Thermal-Magnetic (27) 20A 1P C/B - Thermal-Magnetic

Item No.	Qty.	Catalog Number / Details
		Designation: 1EL1 NQ Panel Interior Location: Top Right - Section 1 208Y/120V 3Ph 4W 60Hz AIR: 10k System Protection: Fully Rated Main Breaker: 100A Aluminum/Copper lugs Mechanical Lugs Bus Bar: Copper Hinged trim Ground Bar: Standard Copper Door Lock w/keys Neutral: Copper Fed from transformer secondary Section 1 - T-1EL1 Phenolic White Surface / Black Letters Nameplate Branch Breakers (4) 15A 1P C/B - Branch Circuit Breaker (20) 20A 1P C/B - Branch Circuit Breaker Designation: T-1EL1 Low Voltage Energy Efficient Transformer Location: Bottom - Section 1 30kVA Three Phase 480V-208Y/120V Aluminum Windings EX30T3H 220 Degree C Insulation, 150 deg C rise Fed from NF Panel Section 1 - 1EH1 Phenolic White Surface / Black Letters Nameplate With the following engineered special feature: TAG number: EX30T3HF Description 1: Substitute above xfmr for Description 2: selected one Quantity Question : 1 With the following engineered special feature: TAG number: 225A480V35K Description 1: add 225A/3P MCB for NF panel Description 2: above to xfmr cell Cable to NF Quantity Question : 1







Front Elevation and Footprint for Equipment Line-Up

Q2C Number

37999262: 3

LEGEND

- FACTORY SUPPLIED CABLE

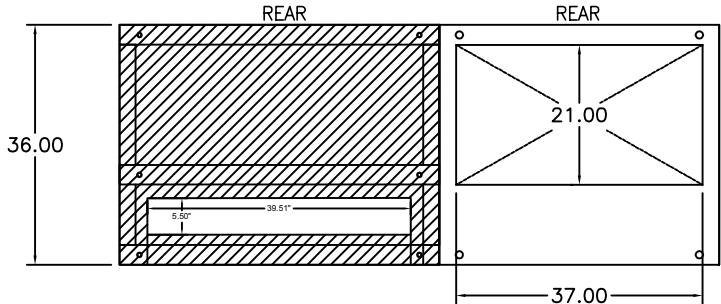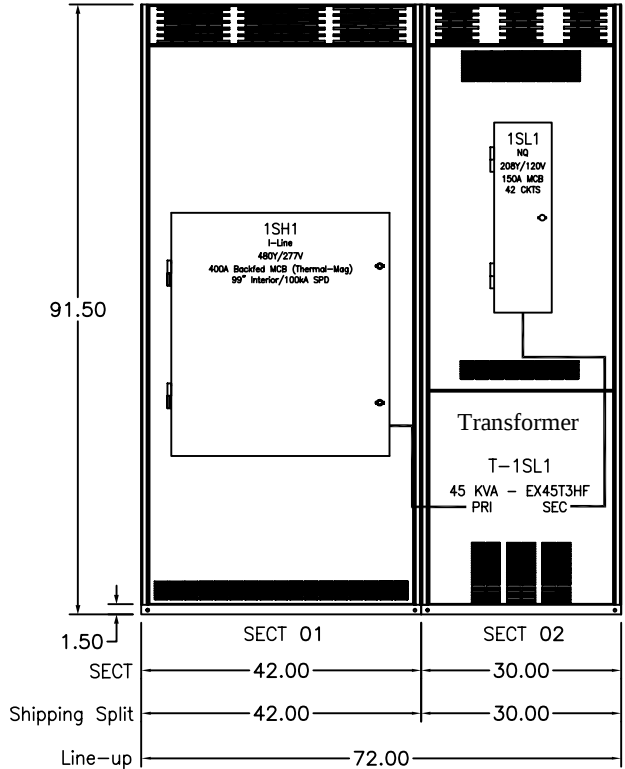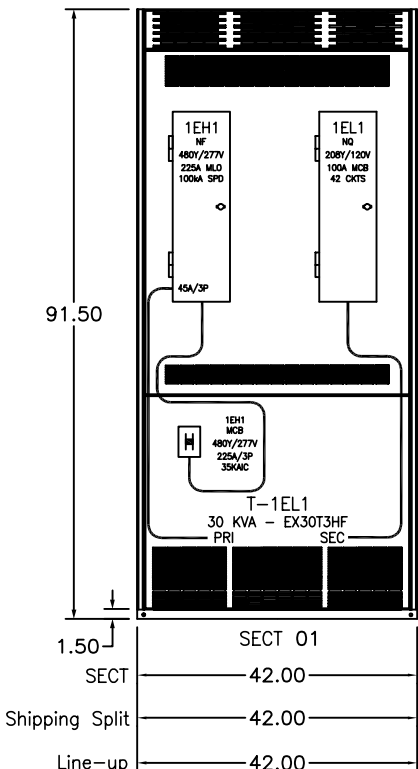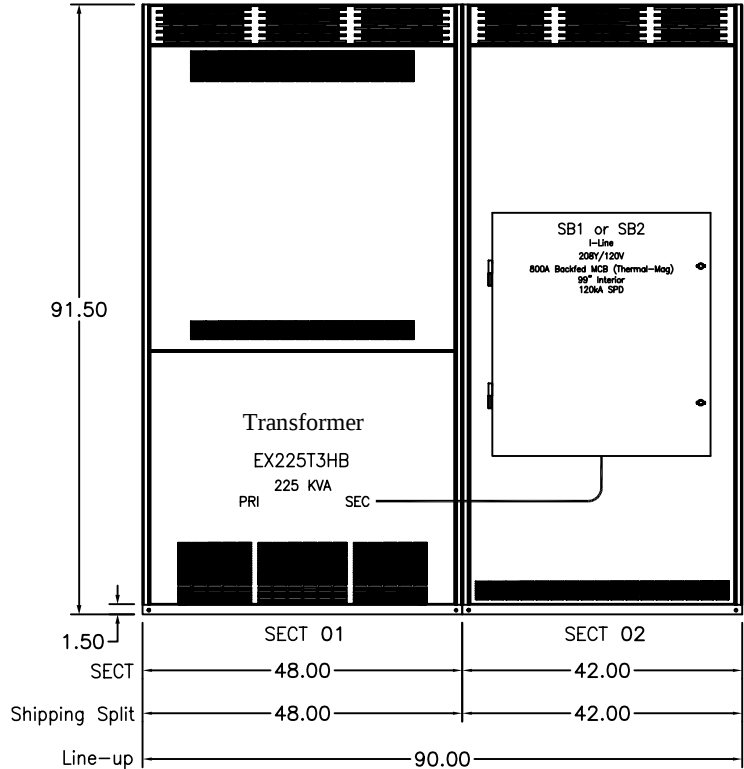

42 X 24 N1/N3R CONDUIT OPENING				
KVA	A	B	C	D
15	4.71	21.63	2.25	6.12
30/45	3.09	21.63	2.25	6.12
75	5.2	7.92	2.25	6.12
112	4.71	8.13	2.25	6.12

INDICATES EQUIPMENT THAT INTERFERES WITH CONDUIT ENTRY

Job Name	Webster University ISB
Job Location	Webster Groves, MO
Drawn By	BES
Engineer	
Date	5/6/2016
Dwg Status	PROPOSAL (NOT FOR CONSTRUCTION)

Equipment Designation	SB1, SB2, 1EH1/1EL1 & 1SH1/1SL1			
Equipment Type	IPC2 (UL891 Rated) - NEMA 1			
Drawing Type	FRONT ELEVATION & FOOTPRINT			
Drawing #		SQUARE D	Page	1 of
		Schneider Electric	REV	0
	113 of 260			

Shop Drawing Submittal Review

Transmitted To: Cannon Design

Date: July 19, 2016

Attention: stl-cac@cannondesign.com

Contact Person / WTA Field Inspector:
Patrick Garner

Project Name: Webster University-**ISB**

Reviewed by: Bill Shaw

Project No. WT 14127.01

☐

UPS

☐

Courier

☒

Email

Copies	No.	Description
1 PDF	264000E01	(Submittal No. 264000-001) Electrical Distribution

Submittal Review Comments

Circuit breaker size and position shall match panel schedules on sheets E0503, 504, 505, & 506.

c: Kelvin Patel
Kpatel@cannondesign.com

☐ Furnish as Submitted

☐ Furnish as Noted

☐ Rejected

☒ ***Revise & Resubmit**

☐ Reviewed

☐

Corrections or comments made on shop drawings during this review do not relieve contractor from compliance with requirements of drawings and specifications. This check is only for review of general conformance with the design concept of project and general compliance with information given in contract documents. Contractor is responsible for: confirming and correlating all quantities and dimensions; selecting fabrication processes and techniques of construction; coordinating his work with that of all other trades; and performing his work in a safe and satisfactory manner.

WTASHOP - Webster ISB - 26 4000-001

From: STL-CAC <STL-CAC@CANNONDESIGN.COM>
To: 'Patrick Garner' <pgarner@wmtao.com>, WTASHOP <wtashop@wmtao.com>
Date: 7/5/2016 11:40 AM
Subject: Webster ISB - 26 4000-001
Cc: "Patel, Kelvin" <kpatel@CANNONDESIGN.COM>, "Grossman, Lynn" <lgrossman@C...>
Attachments: 264000-001 Electrical Distribution.pdf

Attached for review.

Melissa Pirtle
Construction Admin

CANNONDESIGN

1100 Clark Ave
St. Louis, Missouri 63102
T [314.425.8797](tel:314.425.8797) • M
cannondesign.com



77 Westport Plaza
Suite 250
St. Louis, MO 63146

TRANSMITTAL

No. 15051-0114

Paric Corporation

PROJECT: 15051-Webster University Interdisciplinary Science Building

DATE: 07/05/2016

TO: Cannon Design
1100 Clark Ave
St Louis MO 63102

RE: Electrical Distribution

ATTN: Kelvin Patel

JOB: 15051

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
☐ Shop Drawings	☒ Approval	☐ Approved as Submitted
☐ Letter	☐ Your Use	☐ Approved as Noted
☐ Prints	☐ As Requested	☐ Returned After Loan
☐ Change Order	☐ Review and Comment	☐ Resubmit
☐ Plans		☐ Submit
☐ Samples	SENT VIA:	☐ Returned
☐ Specifications	☐ Attached	☐ Returned for Corrections
☒ Other: Product Data	☐ Separate Cover Via:	☐ Due Date:

Item	Package	Code	Rev.	Copies	Date	Description	Status
Submittal		264000-001	1		07/05/2016	Electrical Distribution	Submitted

NOTES:

CC: Paric Corporation, Kathy Bathe

Project Coordinator: Paric Corporation, Kathy Bathe

Signed: _____
Devin Gates

Transmittal

To Paric Corporation

Date 7/1/16

Job Number 11317

Job Name Webster Univ. ISB Building

Attention Devin Gates

Transmittal Number 11317-005

We are sending you:

☒ Attached

☐ Under separate cover, the following:

☐ Preliminary Drawings

☐ Samples

☐ Construction Drawings

☐ Copy of Letter

☐ Specifications

☐ Other _____

Quantity	Drawing #	Date/Revision	Description
1			Submittal for Distribution - Spec Section
			26 40 00

These are transmitted as checked:

☒ For Your Review & Comment

☐ Approved As Noted

☒ For Approval

☐ Returned For Corrections

☐ For Your File

☐ Approved As Submitted

☐ As Requested

☐

Copy:

Transmittal

Enclosure

Rick Branstetter

Signed: Rick Branstetter, Project Manager

Webster University ISB

Approval Drawing Package

Factory Order #: 37999262

06/13/2016

Distributor:
Graybar

Contractor/Installer:
Guarantee Electric / TD4

Consulting Engineer:
Wm Tao & Associates

Lou Feldhaus
Sales Representative

Jake Kaufman
Project Manager
North American Operating Division
(636) 329-2265
jacob.kaufman@schneider-electric.com

Life Is On

Schneider
Electric

TABLE OF CONTENTS

UNIT SUBSTATIONS

BILL OF MATERIALS AND DRAWINGS

UNIT SUBSTATION 1: US-1

METAL-ENCLOSED SWITCHGEAR: US-1

POWER-DRY II TRANSFORMER: US-1

SWITCHBOARD: US-1

UNIT SUBSTATION LITERATURE

Unit Substation Brochure

HVL 5...38 kV Load Interrupter Switchgear - Brochure

Power Dry II- Dry-Type, Small Power Transformer Brochure

Model 98A Digital Temperature Controller For Medium Voltage Transformers

Power-Style QED-2 Switchboard Brochure

Internal Modular SPD Brochure

PowerLogic PM8000 Series Intermediate Metering Technical Data Sheet

NW Breaker Brochure

Micrologic Trip Units for Masterpact Circuit Breakers Brochure

INTEGRATED POWER CENTERS

BILL OF MATERIALS AND DRAWINGS

SB1

SB2

1EH1 - 1EL1

1EL1

1SH1 - 1SL1

LITERATURE

Integrated Power Center 2 (IPC2)

PANELBOARDS

PANELBOARD SCHEDULE AND DRAWINGS

LITERATURE

I-Line Panelboard Handout

NF Panelboard Handout

NQ Panelboard Handout

I-Line SPD

Internal Modular SPD Brochure

SurgeLoc SPD for NQ Panelboards

CONTACTORS AND STARTERS

BILL OF MATERIALS AND DRAWINGS

8538SCG

8538SCA - EF-1

8538SCA - KEF-1

2510FG

LITERATURE

Manual Starters - Type F

Manual Starters - Type M and T

8538 Combination Starter Catalog

SAFETY SWITCHES

BILL OF MATERIALS AND DRAWINGS

D211N

H365

HU361

H361

HU362

POWER MONITORING AND CONTROL

BILL OF MATERIALS

LITERATURE

MCTAS-485 Terminator

FUSE

BILL OF MATERIALS

LITERATURE

LPJ Fuses 1 - 60 Amps

LPJ Fuses 70 - 600 Amps
