



PARIC CORPORATION
77 Westport Plaza Suite 250
St. Louis, MO 63146
TEL: 636-561-9500
FAX: 636-561-9501

REQUEST FOR INFORMATION DATE: September 01, 2016 NO.: RFI-266

To: Cannon Design

Attn: Kelvin Patel

From: Paric Corporation

Requested By: Joe Voypick

Project Name: 15051-Webster University Interdisciplinary Science Building Project No.: 15051

Subject: Conduit Required for Pole Base Ground Cable to ground rod

Response Required By: September 08, 2016

Drawing / Spec Reference:

Information Requested:

Regarding the amount of conduits entering and exiting the type EG5, EG5R and EG3 pole lights;

1. Can we utilize 3/4" conduit in lieu of 1" conduit to run the sight lighting power and control wiring in.
2. Can we run the # 6 bare ground wire with out a conduit, this would eliminate (1) 1" PVC Conduit and help free up needed room in the pole. See attached.

Response:

Provided the code required conduit fill is not exceeded for the current carrying conductors, 3/4" conduit is acceptable where 1" conduit would be too difficult to install.


Regarding the ground conductor, provide a 1/2" PVC conduit in-lieu of the 1" conduit.

ARCHITECT'S RESPONSE:

This information is provided as an interpretation of the Contract Documents for implementation. It is not an authorization for change to the Contract Sum or Contract Time. If this information results in a claim for a change to the Contract, the Contractor shall notify the [Construction Manager][Architect] of a change through the change process.

Answered By: Mark de la Fuente, WTA

Date: 9/6/16

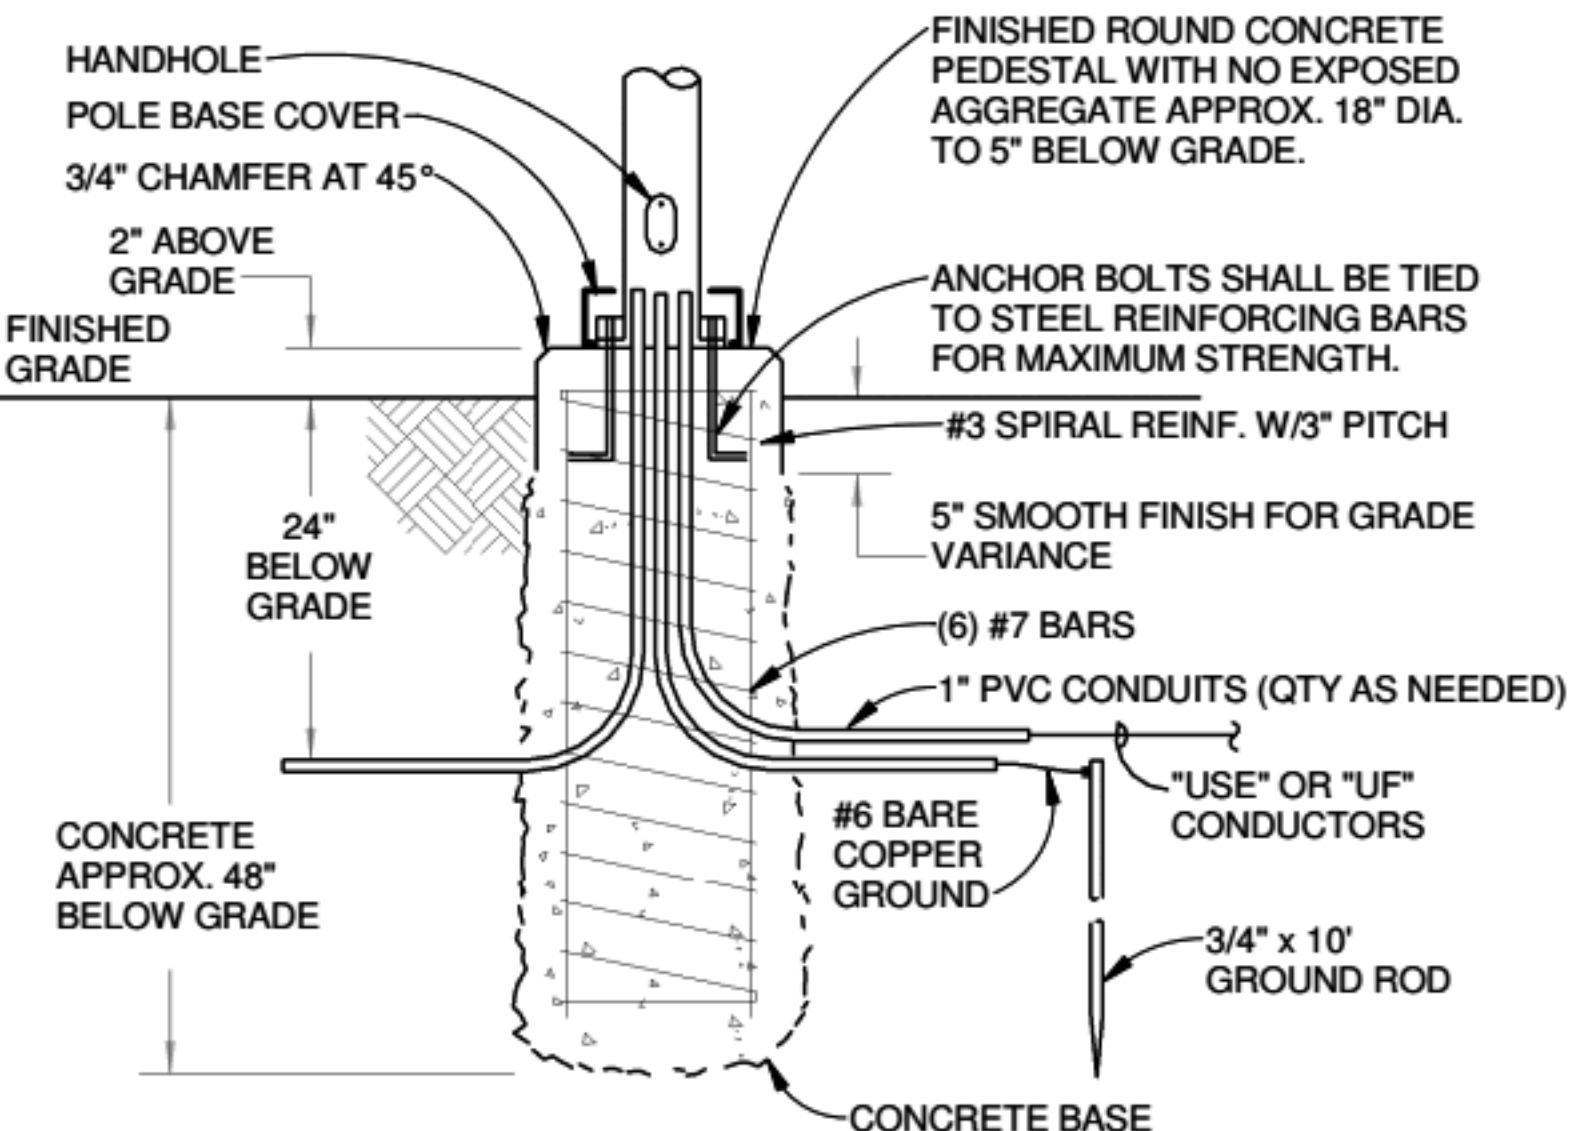

LIGHTING POLE "EG" CONCRETE BASE DETAIL

APPLIES TO ALL POLE MOUNTED LIGHTS UNLESS OTHERWISE INDICATED.
PROVIDE ADDITIONAL 1" PVC CONDUITS TO DIMMABLE 0-10V FIXTURES.
SUBMIT PRE-MANUFACTURED STEEL REINFORCING CAGE FOR APPROVAL.
