



PARIC CORPORATION
77 Westport Plaza Suite 250
St. Louis, MO 63146
TEL: 636-561-9500
FAX: 636-561-9501

REQUEST FOR INFORMATION	DATE: October 10, 2016	NO.: RFI-321
--------------------------------	-------------------------------	---------------------

To: Cannon Design

Attn: Kelvin Patel

From: Paric Corporation

Requested By: Devin Gates

Project Name: 15051-Webster University Interdisciplinary Science Building	Project No.: 15051
---	--------------------

Subject: Existing drain lines at EAB

Response Required By: October 17, 2016

Drawing / Spec Reference:

Information Requested:

There are existing drain tile lines at the north of the EAB (see attached photos) that were dug up during demo of the stairs. Paric proposes to tie them into the storm sewer to the east as shown in the attached sketch. Please advise if this will be acceptable.

There is a drain in the portico on the north of the EAB which currently drains to the exterior of the building. Paric proposes to reroute the drain into an existing drain on the west of the building (see attached photo) and remove the drain line exiting the north of the building. Please advise if this will be acceptable.

Response:

Both suggestions are acceptable.

ARCHITECT'S RESPONSE:

This information is provided as an interpretation of the Contract Documents for implementation. It is not an authorization for change to the Contract Sum or Contract Time. If this information results in a claim for a change to the Contract, the Contractor shall notify the [Construction Manager][Architect] of a change through the change process.


Answered By: Mark Davis

Date: 10/24/2016



PROPOSE TO TIE
INTO STORM
LINE

NERINX HALL

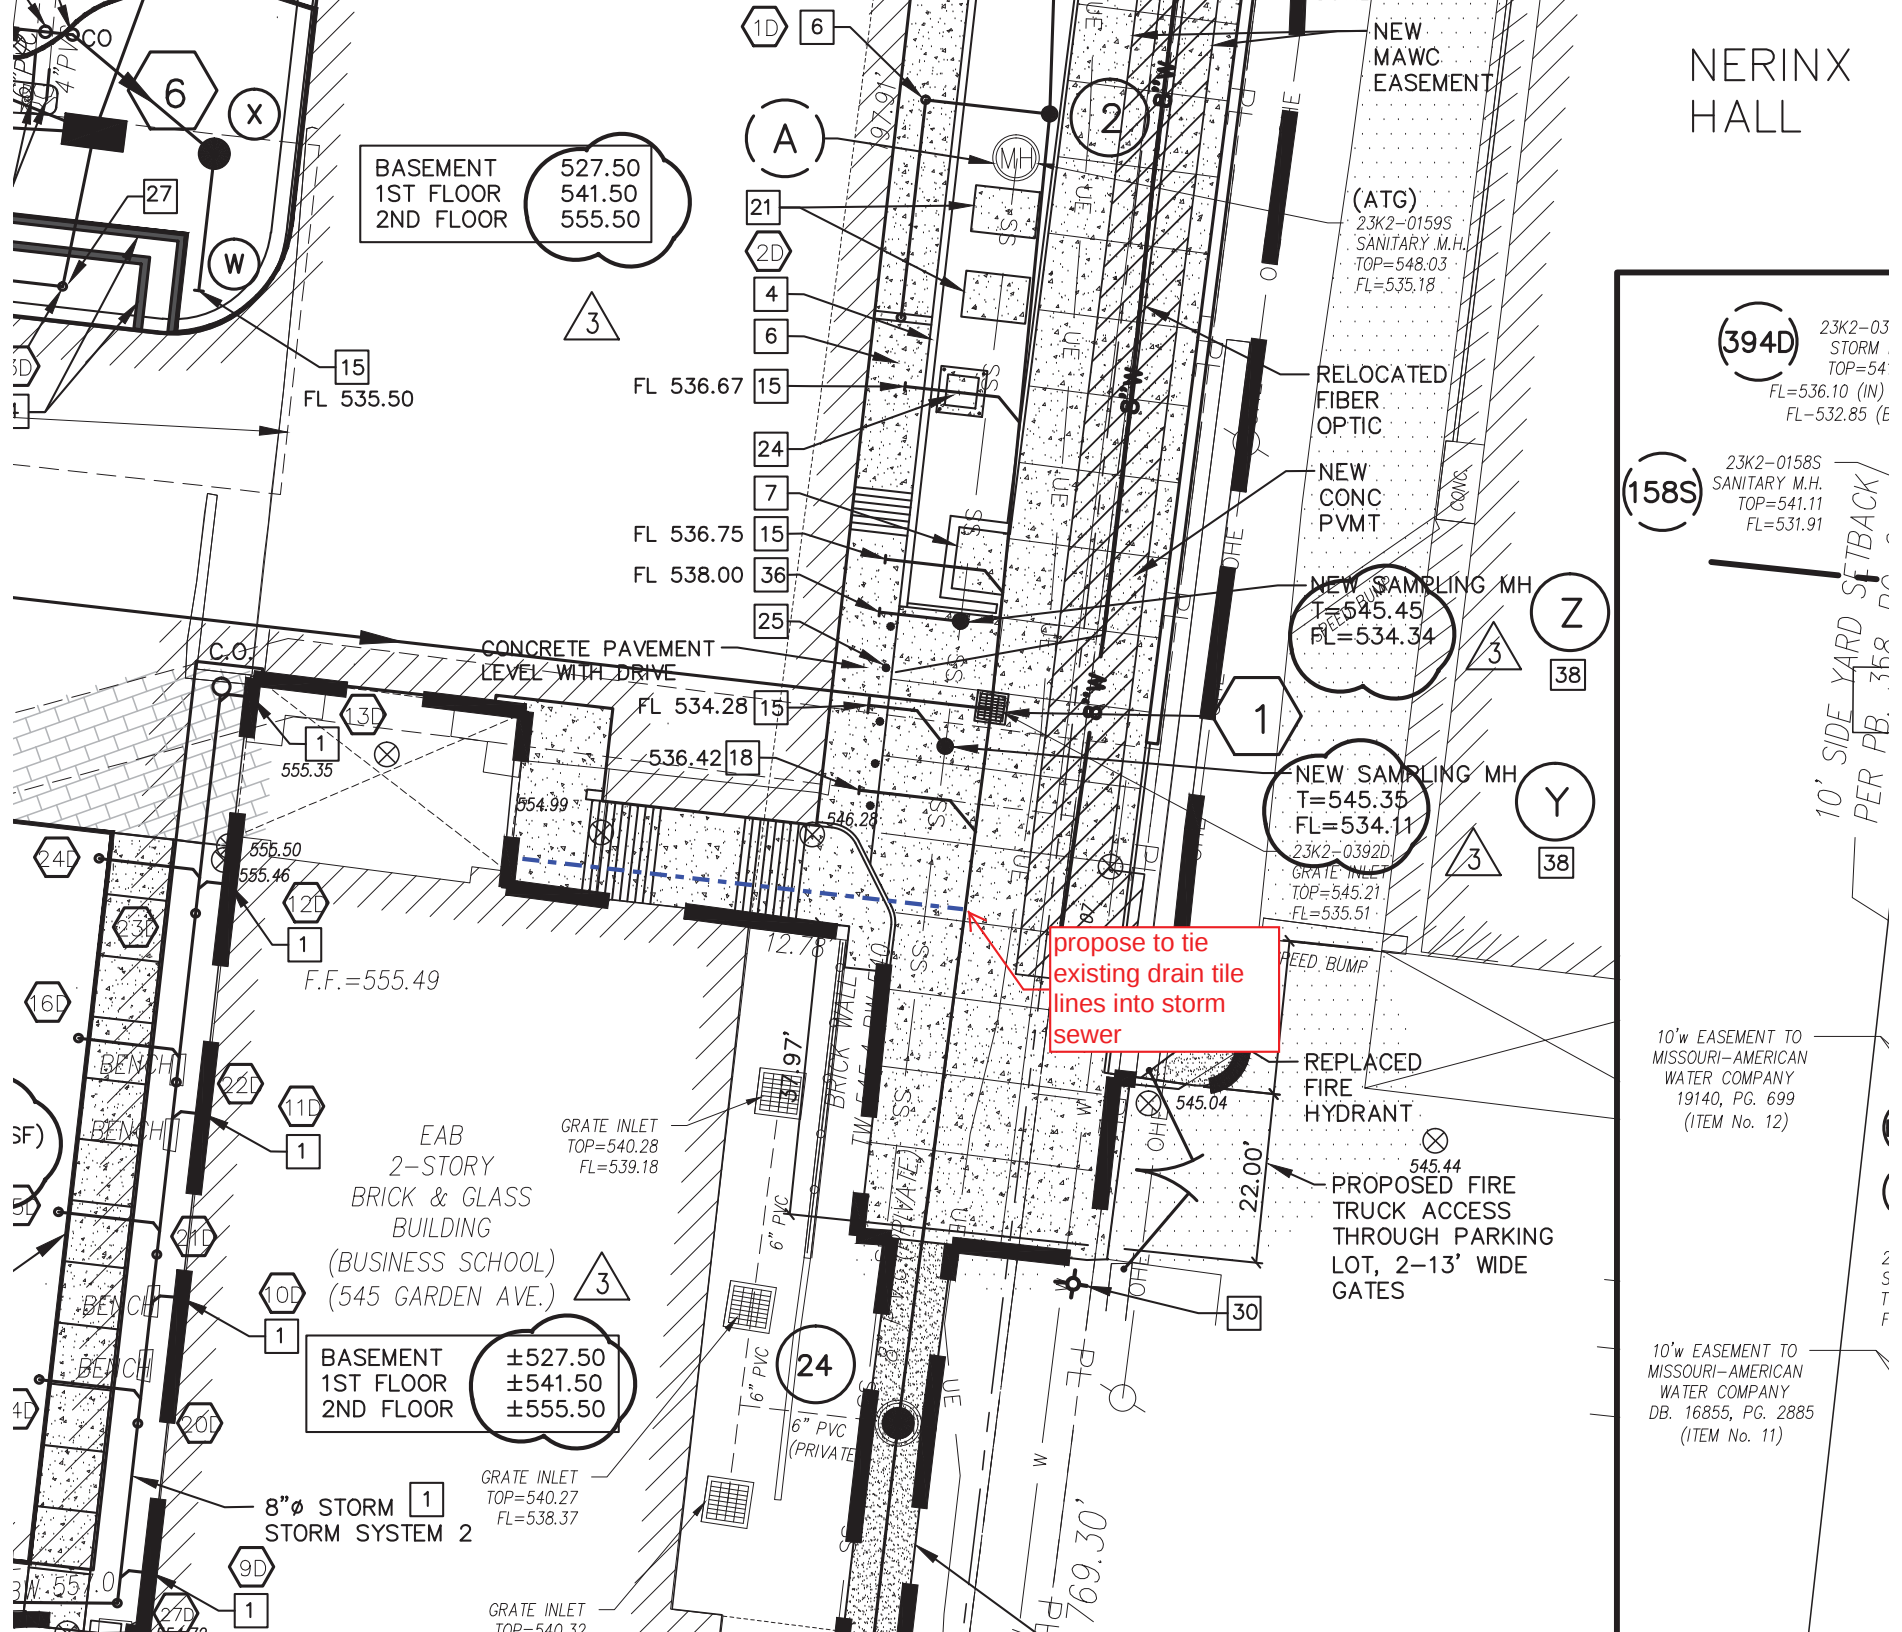

PROPOSE TO TIE
DRAIN INTO
ALTERNATE
INTERIOR LINE
(SEE OTHER
PHOTO) AND
PATCH HOLE.



PROPOSE TO
CUT PORTICO
DRAIN LINE AND
TIE INTO
EXISTING LINE
AS SHOWN

