PRECAST DIVISION

PROJECT Webster Univ

SUBJECT MH Y

CUSTOMER Castle

DATE SUBMITTED BY BH

CHKD SHEET NO. OF

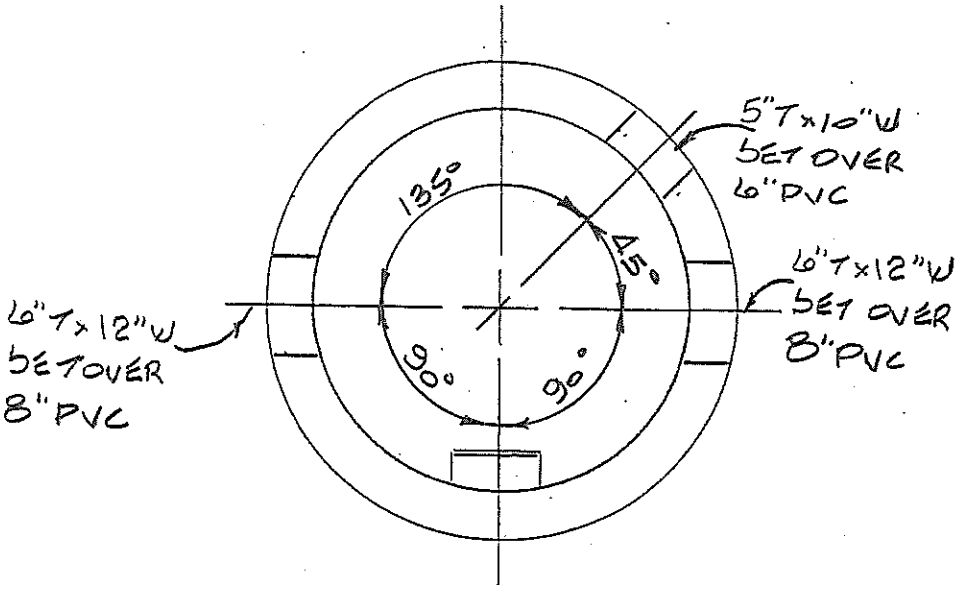


TOP 545.35
FL 534.11

R-1775 F & C
36" MSD Cone
36" Riser

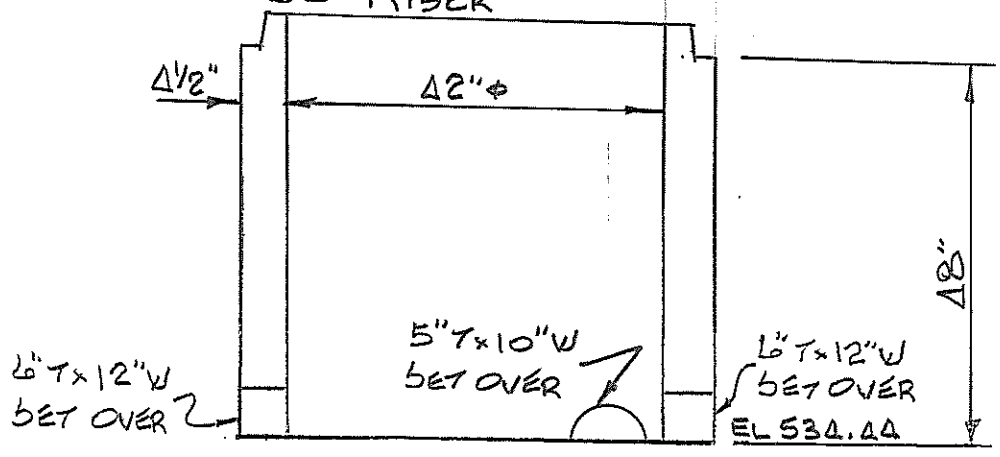

PRECAST DIVISION

PROJECT WEBSTER UNIV

SUBJECT MH 2

CUSTOMER CASTLE

DATE SUBMITTED BY BH

CHKD SHEET NO. OF

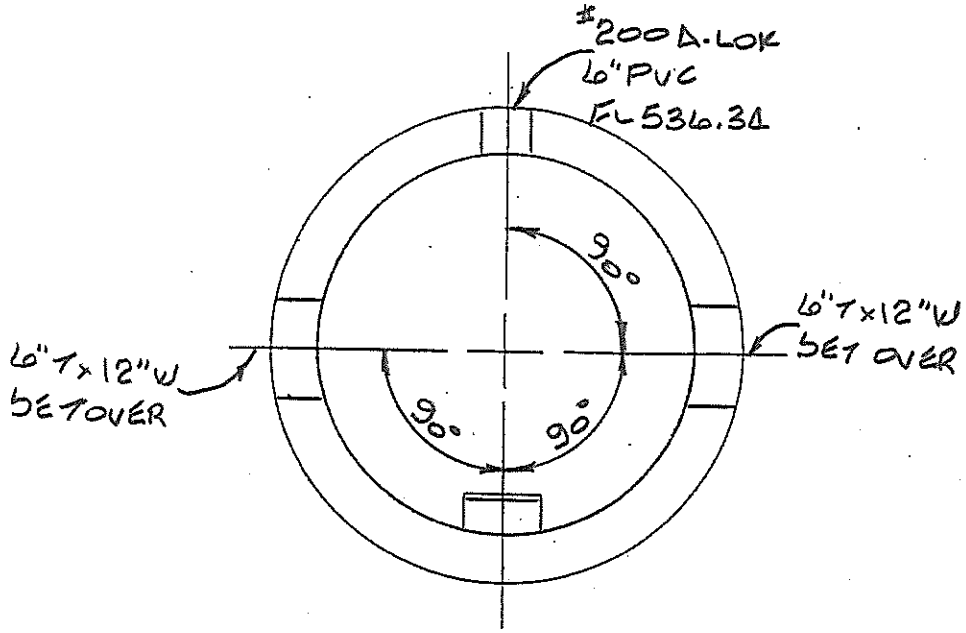


TOP 545.45
FL 534.34

R-1775 F & C
36" MSD CONE
36" RISER

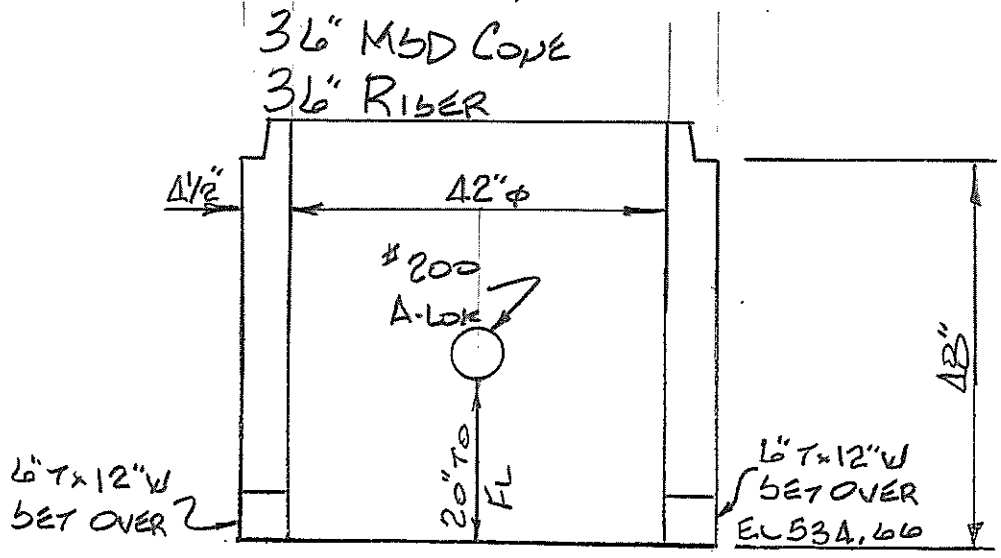

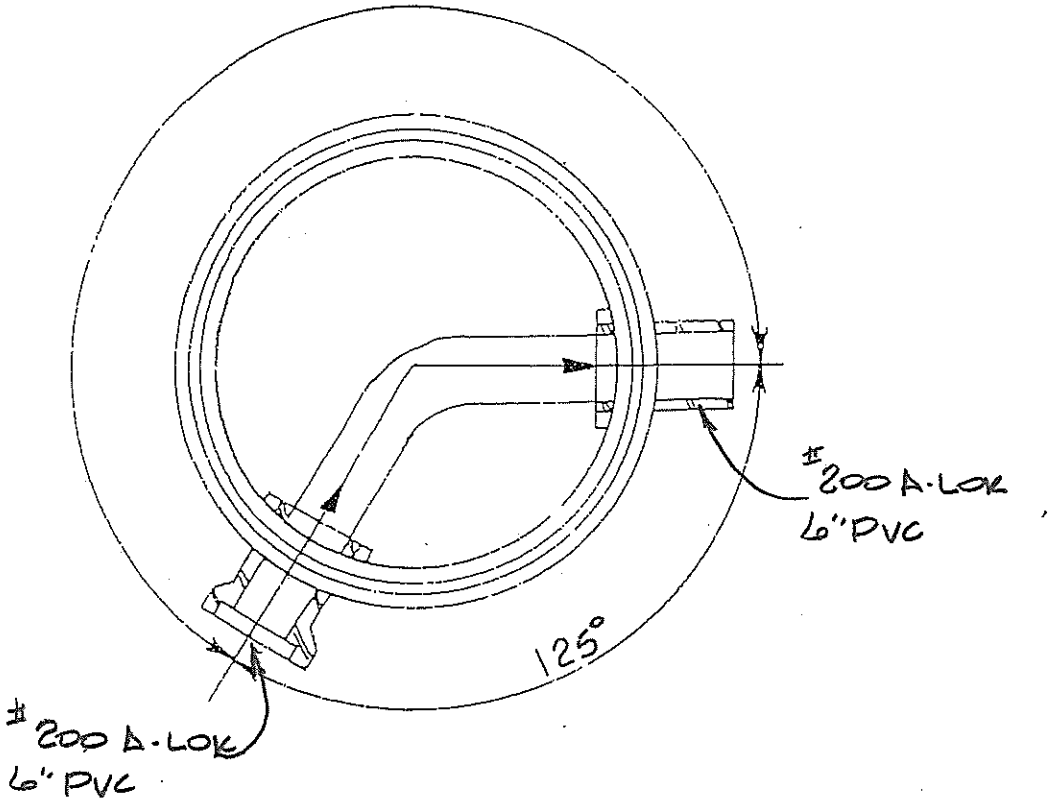


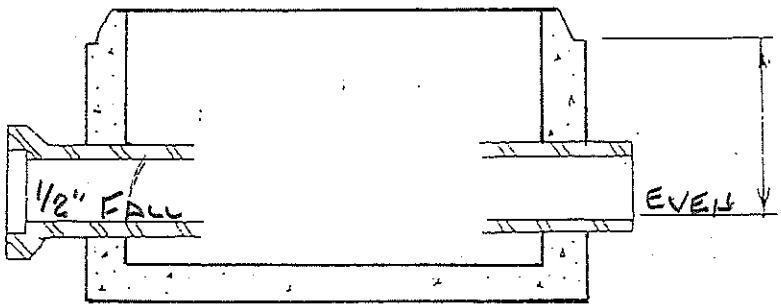


3-
24"
48

R-1775 F & C
4" COLLAR
15" MED CONE
36" DROP
48" RISER
48" RISER
22" BASE

TOP 551.00
INV 535.86

SIZE OF STRUCTURE:

42" ϕ

PRECAST DIVISION

PROJECT WEBSTER UNIV
SUBJECT MH X
CUSTOMER CASTLE
DATE SUBMITTED BY BH
CHKD SHEET NO. OF

PRECAST DIVISION

PROJECT Webster Univ

SUBJECT MH X

CUSTOMER Castle

DATE SUBMITTED BY BH

CHKD SHEET NO. OF

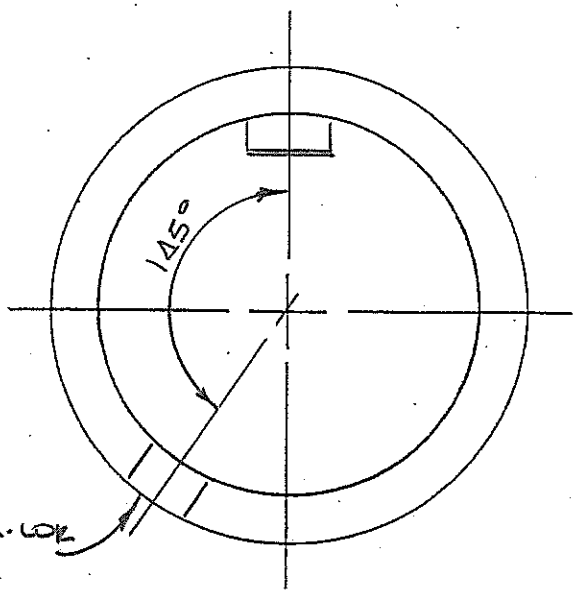


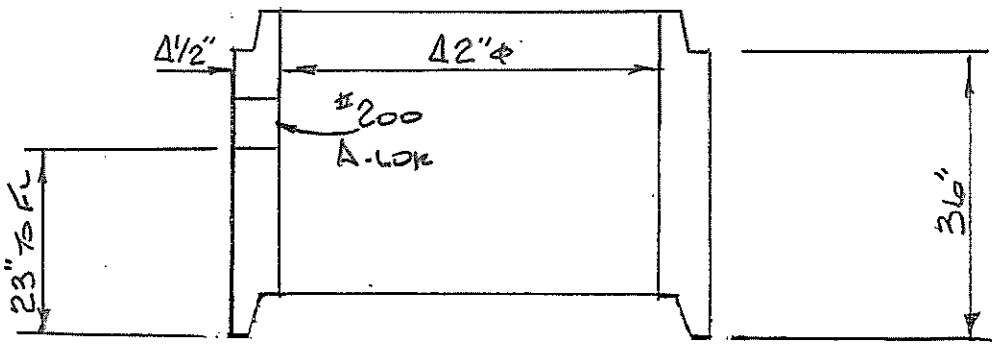

CANNONDESIGN

# SUBMITTAL IDENTIFICATION SHEET

**To be completed by Contractor/CM**

WEBSTER UNIVERSITY ISB
PROJECT NAME

8274 BIG BEND BLVD
ADDRESS

NUMBER

WEBSTER UNIVERSITY
OWNER

CANNON DESIGN
ARCHITECT / ENGINEER

Joe Voypick
SUBMITTED BY

221313-007
CONTRACTOR / CM SUBMITTAL NO.

CANNON DESIGN SUBMITTAL NO.

DRAWING / DETAIL REFERENCE

221313
SPECIFICATION SECTION / PARAGRAPH

Castle Contracting
MANUFACTURER / SUPPLIER

ITEM / PRODUCT ID

REQUIRED DATE

PRIORITY

◯ CRITICAL

ITEM BEING SUBMITTED (check only one)

- ◉ Shop Drawings
- ◯ Samples ( _____ copies)
- ◯ LEED Submittal
- ◯ Certification / Qualifications
- ◯ Record Documents
- ◯ Product Data
- ◯ Coordination Drawing
- ◯ Calculations
- ◯ Schedules
- ◯ O&M Manuals
- ◯ Other _____

ITEM BEING SUBMITTED FOR (check only one)

- ◉ Action
- ◯ Information Only
- ◯ Record

REMARKS OR DEVIATIONS

CONTRACTOR / CM CERTIFICATION
(SUBMITTALS NOT CERTIFIED WILL BE RETURNED WITHOUT REVIEW)

PARIC

PARIC CORPORATION
SUBMITTAL STAMP

THIS SHOP DRAWING HAS BEEN REVIEWED BY PARIC CORPORATION

Subcontractor remains responsible for dimensions, quantities, coordination with other trades and compliance with contract documents.

By:
Devin D. Gates

Joe Voypick
REVIEWED BY

8/29/16
DATE

**To be completed by Reviewer**

22 1313-007
CANNON DESIGN SUBMITTAL NUMBER

8/30/16
RECEIVED DATE

- ◉ A. No Exceptions Taken
  No further review of submittal is required.
- ◯ B. Make Corrections Noted
  Incorporate corrections in work; resubmission is not required.
- ◯ C. Revise and Resubmit
  Revise as noted, and resubmit for review.
- ◯ D. Rejected
  Submittal is not in compliance with Contract Documents; provide new submittal.
- ◯ E. For Record / Information Only
  Submittal was reviewed for Record / Information purposes only.
- ◯ F. Not Required for Review
  Submittal is not required by Contract Documents and has not been reviewed.

Review is for conformance with the design concept of this project and for general compliance with contract documents. Contractor is responsible for quantities, dimensions and compliance with contract documents and for information that pertains to fabrication processes, construction techniques and coordination of this work with all trades which will be affected thereby. This review is null and void if submittal deviates from contract documents and does not indicate or note deviations.

A/E COMMENTS

◯ See attached sheet(s) for additional comments

Mark Davis
Digitally signed by Mark Davis
DN: CN=M. D.=mdavis@davidmason.com, O=David Mason and Associates, OU=Civil, CN=Mark Davis
Location: St. Louis
Reason: I am the author of this document
Contact Info: 1-314-534-0200
Date: 2016.08.31 11:26:00-05'00'
REVIEWED BY

08/31/2016
DATE

77 Westport Plaza
Suite 250
St. Louis, MO 63146

# TRANSMITTAL

**No. 15051-0200**

*Paric Corporation*

**PROJECT:** 15051-Webster University Interdisciplinary Science Building

**DATE:** 08/29/2016

**TO:** Cannon Design
1100 Clark Ave
St Louis MO 63102

**RE:** Precast Sanitary Structure Shop Drawings

**ATTN:** Kelvin Patel

**JOB: 15051**

| WE ARE SENDING: | SUBMITTED FOR: | ACTION TAKEN: |
|---|---|---|
| ☑ Shop Drawings | ☑ Approval | ☐ Approved as Submitted |
| ☐ Letter | ☐ Your Use | ☐ Approved as Noted |
| ☐ Prints | ☐ As Requested | ☐ Returned After Loan |
| ☐ Change Order | ☐ Review and Comment | ☐ Resubmit |
| ☐ Plans | | ☐ Submit |
| ☐ Samples | **SENT VIA:** | ☐ Returned |
| ☐ Specifications | ☐ Attached | ☐ Returned for Corrections |
| ☐ Other: | ☐ Separate Cover Via: | ☐ Due Date: |

| *Item* | *Package* | *Code* | *Rev.* | *Copies* | *Date* | *Description* | *Status* |
|---|---|---|---|---|---|---|---|
| Submittal | | 221313-007 | 1 | | 08/29/2016 | Precast Sanitary Structure Shop Drawings | Submitted |

**NOTES:**

**CC:**

**Signed:** _____

Devin Gates

CASTLECONTRACTING

# SUBMITTAL TRANSMITTAL

345 Marshall Avenue Suite 302, Webster Groves, MO 63119
314-421-0042 phone, 314-231-9157 fax

**To:** Jason Szachnieski
Paric Corporation

**From:** Ethan Gwinn
**Date:** 8/29/2016

**Attn:**

**Project Name:** Webster ISB
**CASTLE Project Number:** 83160.106
**Architect/Engineer's Project Number:**

**Subm. #:** 6 **Sub/Vendor:** Kienstra Precast

**PLEASE FIND ENCLOSED:**

| Copies | Date | No. | Description |
|---|---|---|---|
| 1 | 8/29/2016 | 1 | Precast Sanitary Structures |
| | | | |
| | | | |
| | | | |
| | | | |

**ACTION:**

| | | | |
|---|---|---|---|
| X | For Approval | | Approved As Submitted |
| | For your Use | | Approved As Noted |
| | As requested | | Revise & Resubmit |

**COMMENTS:**

*CC:* File
